



Hilliard Road Bridge Rehabilitation Update

Nichole English, PE


CUY-Hilliard Road Bridge 08.57 Rehabilitation

(PID 109594)

8/24/2026



Location

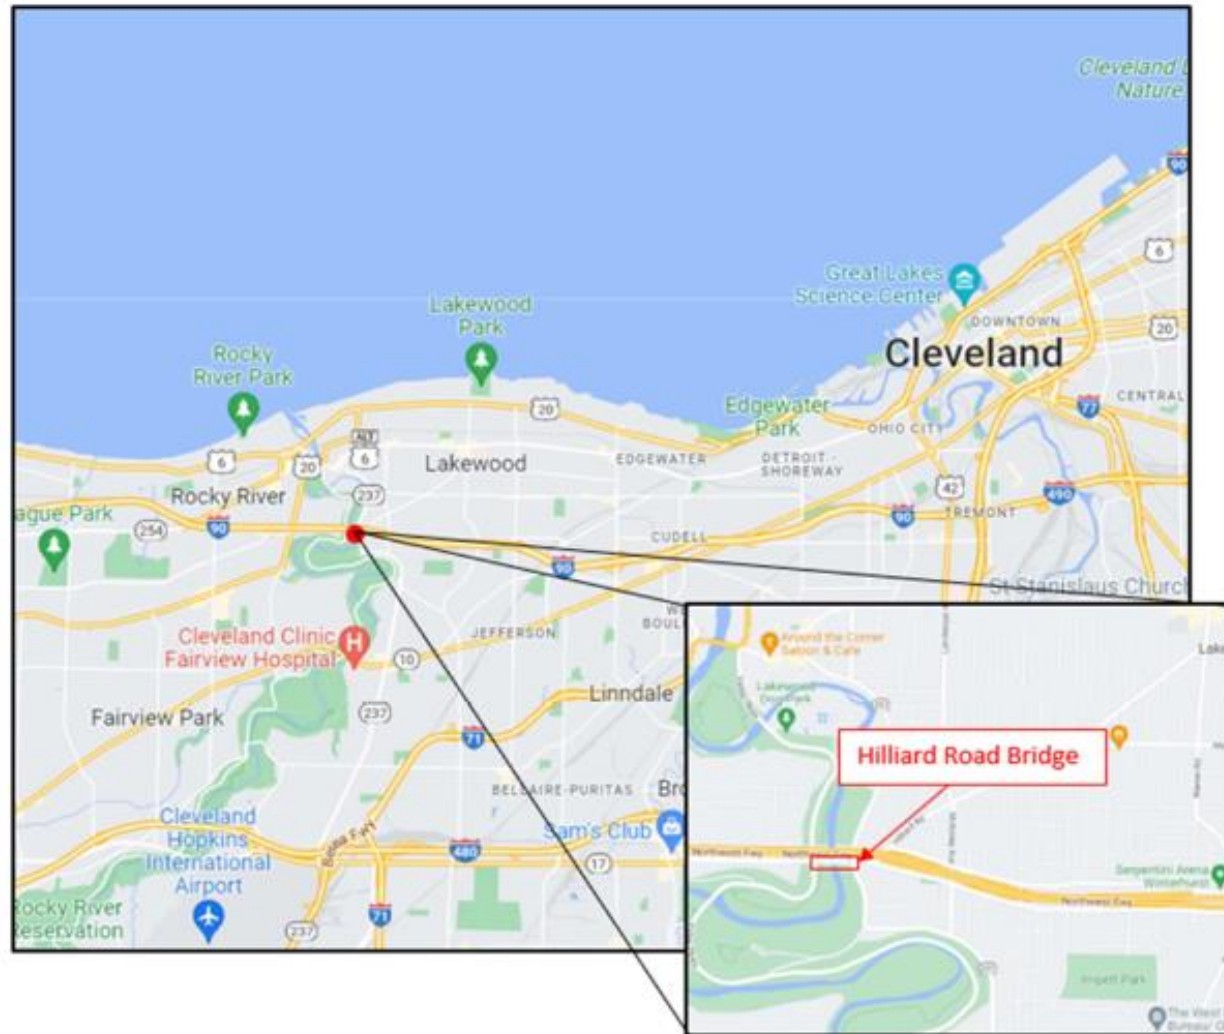

Existing Bridge Conditions



Project Timeline (Updated)

2022-24

- Feasibility Study completed
- Single span steel arch bridge proposed
- Cost Estimates rose from \$57M to \$87M

2025

- Consensus to move forward on steel girder bridge type
- Consultant given NTP for Stage 1

2026

- Stage 2 Plans in December
- Public Engagement on-going
- Final R/W started

2027


- Stage 3 Plans in March
- Final Plans in September

2028


- Begin Construction
- End Construction December 2030



Existing vs. Proposed Bridge

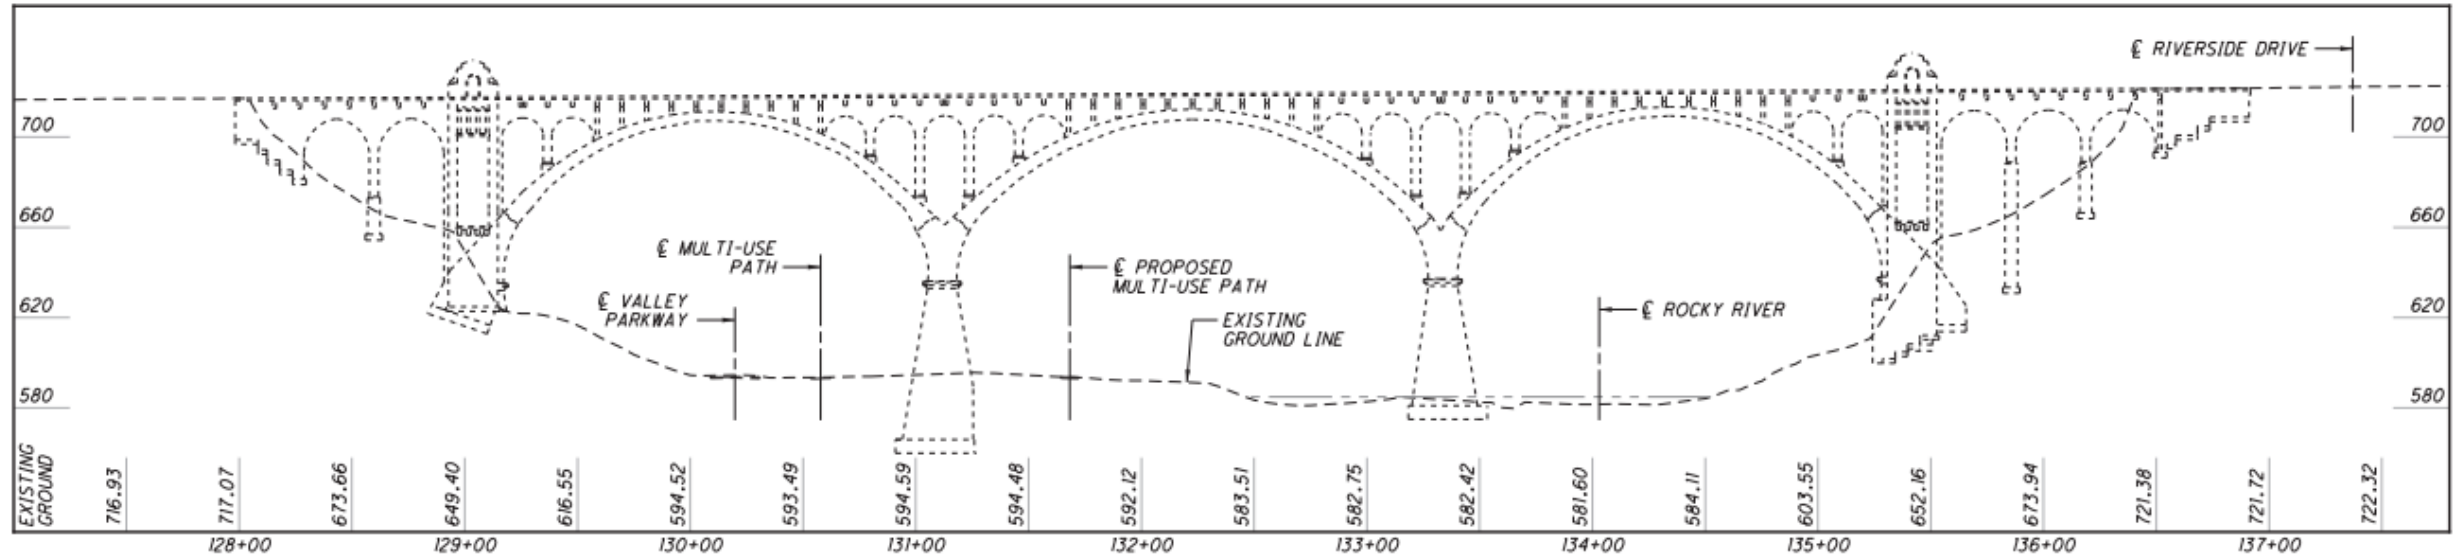


PROFILE ALONG ∇ CONSTRUCTION HILLIARD ROAD - EXISTING BRIDGE

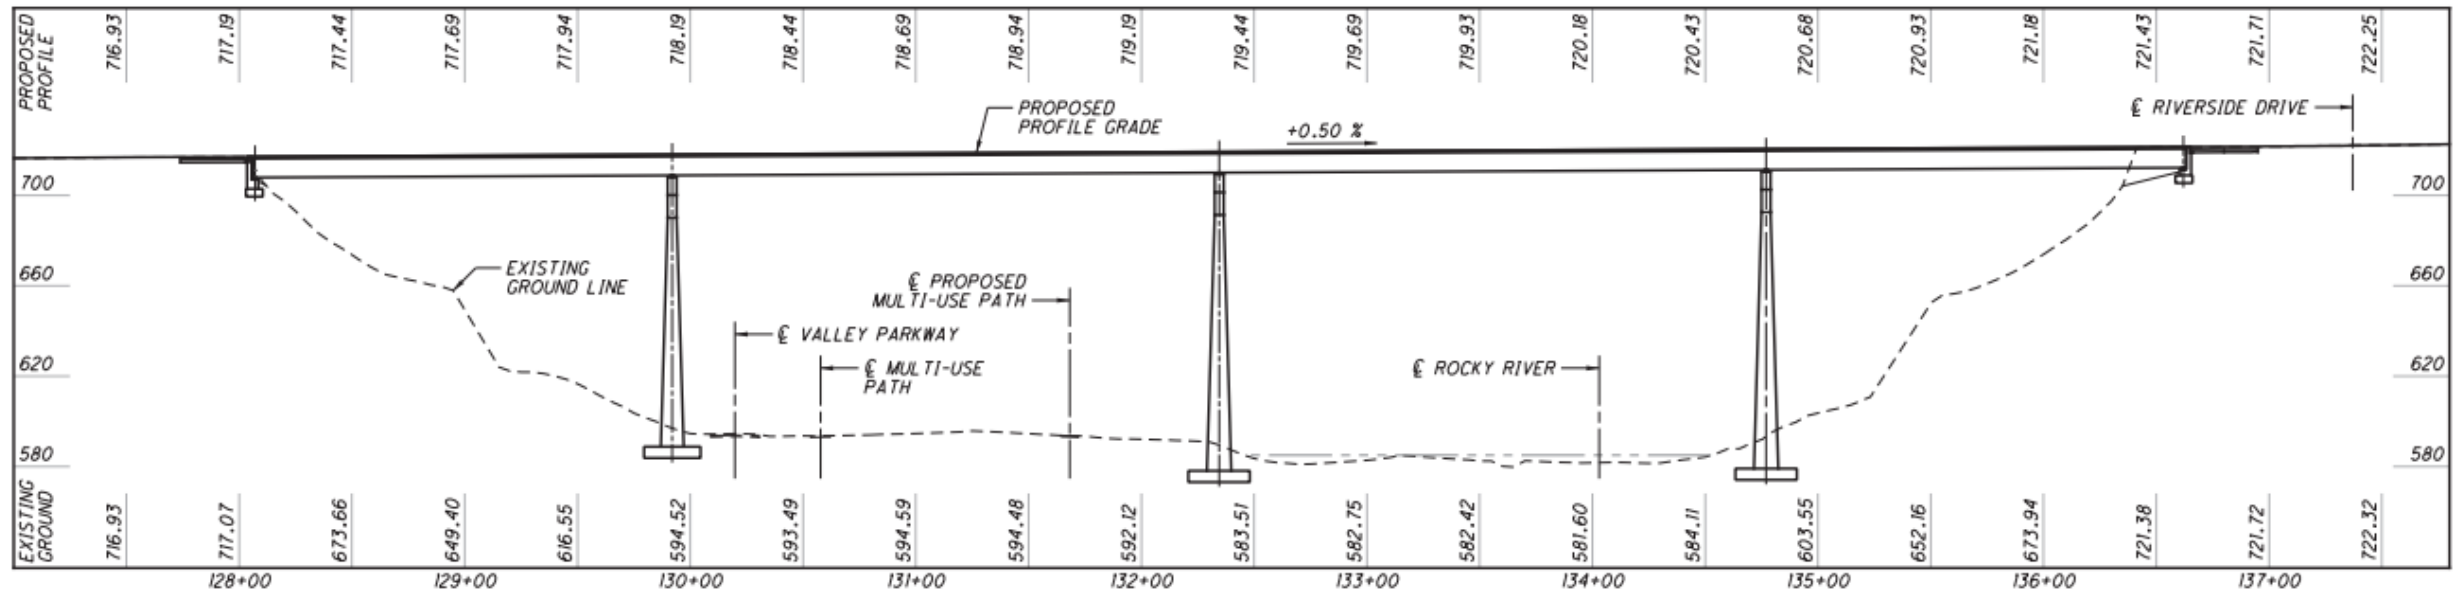

PROFILE ALONG ∇ CONSTRUCTION HILLIARD ROAD - ALTERNATIVE 1 (STRAIGHT STEEL PLATE GIRDERS)



Proposed Project - unchanged

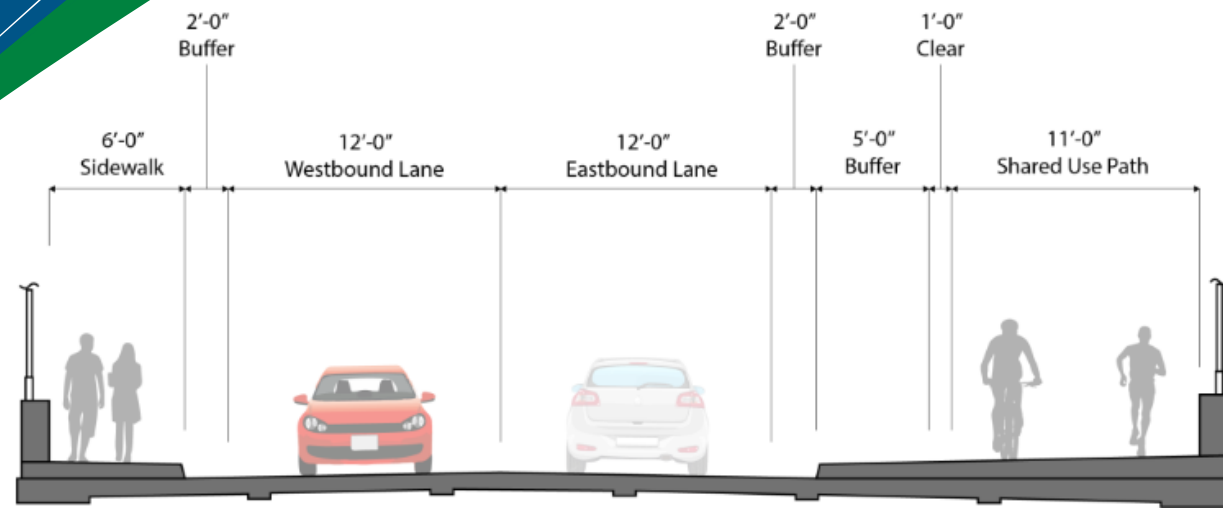

Proposed Project (cont.)



Current Cost Estimate

Task	Total Cost	Federal	Local	Unfunded
Planning and Design	\$7,205,192	-	\$7,205,192	-
Right of Way	\$500,000	-	\$500,000	-
Construction	\$59,946,997	\$32,316,175	\$10,000,000	\$17,630,822
Construction Engineering	\$4,795,760	-	\$2,426,582	\$2,369,178
Total	\$72,447,949	\$32,316,175	\$20,131,774	\$20,000,000



Secured Project Funding

Funding Source	Amount	Status
ODOT local major bridge	\$19,816,175	FY 2028
NOACA federal STBG	\$12,500,000	FY 2028

Other investigated funding opportunities – County road & bridge, Federal BIP, OPWC, NOACA TIP, CEAO local bridge



Recent Public Involvement

- Public Virtual Open House
- Targeted Outreach
- June 25, 2026 – July 27, 2026
- 56 Responses
- 33 Requests to be Consulting Parties

Bike & Pedestrian Path
National Register
Four Lanes
Emergency Vehicles
Funding
Arch
Chain-Link Fence
Cost
Two Lanes
Shared-Use Path
Maintenance & Lifespan
Public Involvement
Traffic & Safety
Historic Preservation
Environmental Impacts
Peregrine Falcons



Aesthetic Enhancement

Commitments

- Scenic Overlooks
- Decorative Lighting
- Decorative Railing
- Relocating Valley Trail

Additional Opportunities

- Pier Form Liner / Graphics
- Interpretive Signs



Vrooman Road Bridge (ODOT D12)



Key Project Milestones

- Funding
 - September 2026 – OPWC Application Due
 - October 2026 – Draft NOACA TIP Introduction
- Design
 - December 2026 – Stage 2 Plan Submittal
 - January 2027 – Final R/W Plan Submittal
 - May 2027 – Stage 3 Plan Submittal
 - October 2027 – Plan Package Submittal to Central Office
- Construction
 - February 2028 – Bid Opening
 - April 2028 – Award/Construction Begins
 - December 2030 – End Construction



